

## **Fellowship Hall Kitchen Update – Scroll down for the progress!**

May 8, 2018

Work started this week and here's the first of our progress reports...

#demoday pics below—maybe we'll get our own cable TV show!



Matt and Jack from “Restaurant Rescue” began by taking apart appliances in the kitchen. Most of the pieces are being cut up and recycled; some of the stainless-steel tables will be re-used in the new kitchen set-up.

We are re-doing the church kitchen to meet Commercial Kitchen standards. Intense planning and choreography are driving the project because it needs serious upgrades to surpass modern building codes for utilities and infrastructure standards.



Demolition of the wooden cabinets in the kitchen came next because wood doesn't meet code for modern commercial kitchens. It was a messy job but the crew from DRD Services made quick work of it. Below, the same view after an hour of heavy lifting.





The dumpster is loaded, and away it goes!

May 14—Asbestos Abatement begins...



May 21 – Asbestos Abatement complete...ready for work to begin!



July 18, 2018

Contractors selected, contracts signed, and work begins...

First, the electrical re-routing:




And the new gear waiting its turn:



It's hard to tell in the picture, but all this gear takes up half the room!

August 6, 2018

First, the plans...keep scrolling for more.

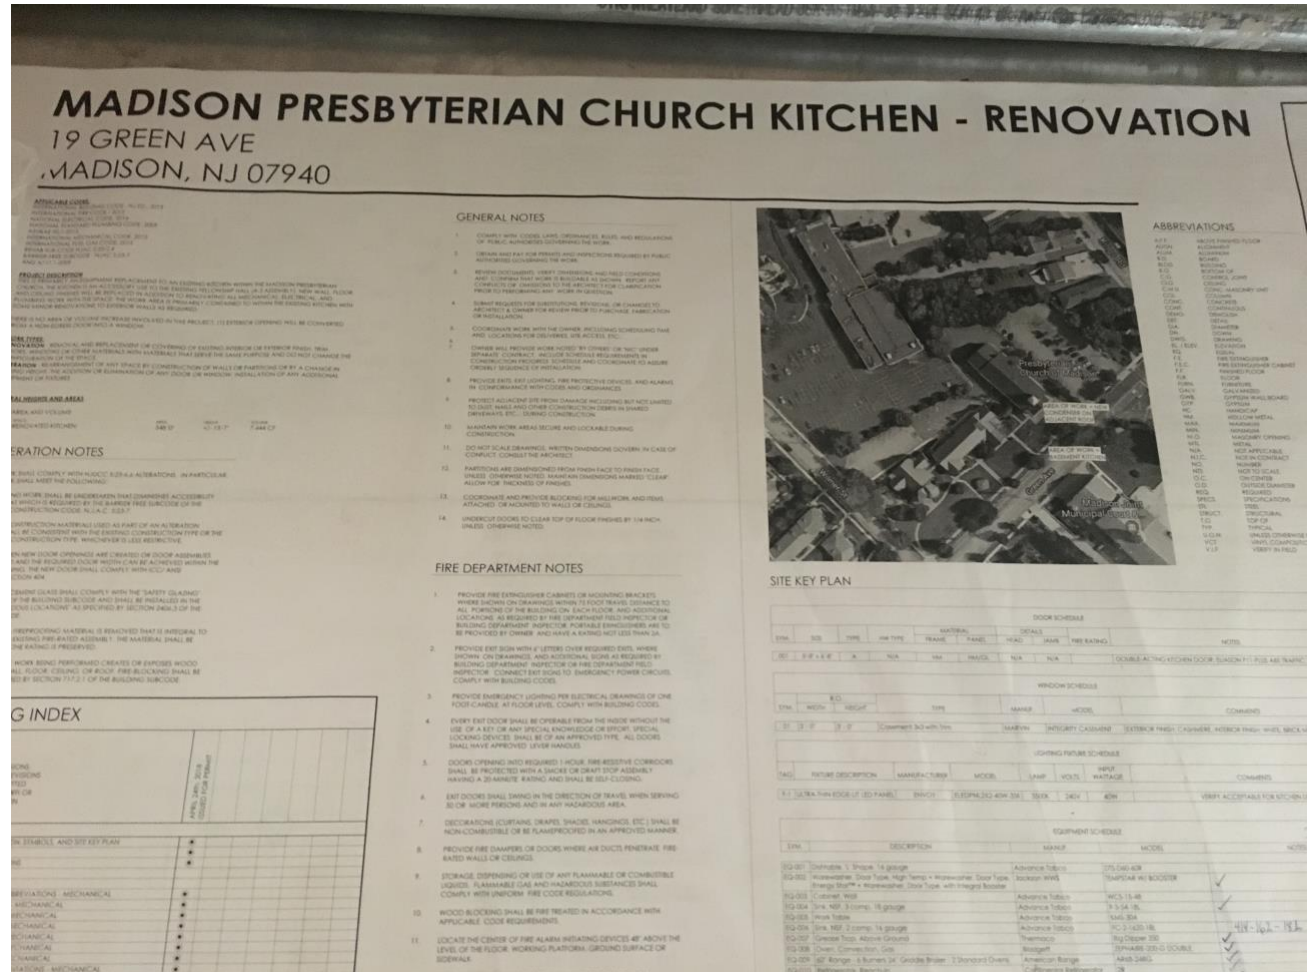

Exhaust hood installed, and plumbing work is moving along. You can see the big trenches to accommodate the plumbing...



And all that gear is starting to get unpacked!



October 24, 2018

Finally! It's starting to look like something after a couple months of trouble-shooting termite damage, slab work, plumbing, and electrical. We're getting there!





